


Facility Construction Project Photos – June 2024

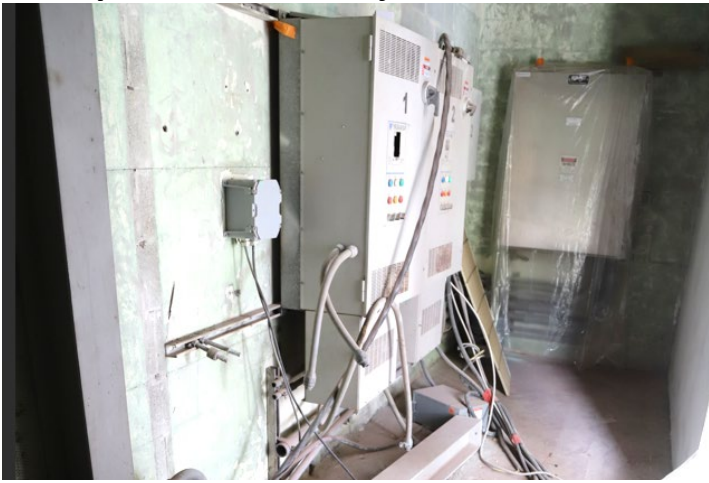

1. Southwest view of the existing PS4002 – exterior painting activities ongoing.
2. View of the interior loading dock painting activities.
3. View of the instrumentation and electrical control room—structural repairs and painting activities are pending the delivery of the electrical components before the existing equipment is taken offline and the system placed on JWSC sewer bypassing.
4. View of the lower-level dry pit – piping and equipment protected while painting activities are ongoing.
